

Colonial Road Runners Frosty Half-Marathon Raynham, MA

Measured on Nov 17, 2017 by Mark Capparella
Tri-Valley Front Runners (TVFR)
E-mail: mark_capparella@waters.com
Tel: 508 740 7836

Course Description (given in reference to the direction of the race)


START on main access road to Raynham Middle School as per START DETAIL heading south onto Titicut Rd.
Follow Titicut Rd to end and turn LEFT onto WhiteSt.
LEFT onto Pleasant St. - MILE 1 is 5'8" after trailing edge of storm grate at corner of White St.
RIGHT onto Locust St. - MILE 2 is 18'7" after end of guard rail on right side of road across from 80 Locust St. - MILE 3 is 6'6" after utility pole TMLP 4 on Locust St at corner of King St.
5K is 88'6" before mailbox for 630 Locust St.
LEFT onto Forest St., RIGHT onto Leonard St.
MILE 4 is 13'8" before utility pole TMLP 3 on Leonard
RIGHT onto Judson St. - MILE 5 is 20'6" after NET&T Co utility pole 57 on Judson
RIGHT onto Tearall Rd. - MILE 6 is 36' before leading edge of first curb at corner of Buck Knoll
LEFT onto Buck Knoll Rd., LEFT onto Deer Hollow
10 K is 1'6" before fire hydrant cross from 116 Deer Hollow.
RIGHT onto Tearall Rd. , RIGHT onto Judson St.
MILE 7 is 5'6" after trailing edge of storm grate in front of 185 Judson St.
RIGHT onto Orchard St. - MILE 8 is 18' after trailing edge of storm grate in front of 295 Orchard St.
RIGHT onto Miller Terrace. , RIGHT onto King St.
MILE 9 is 9' after mailbox for 539 King St.;
15K is 40'6" before mailbox for 722 King St.
LEFT onto Locust St. - MILE 10 is 50'8" before utility pole TMLP 44 on Locust St.
LEFT onto Pleasant St. - MILE 11 is 78' before first storm grate on left side of road on Pleasant
RIGHT onto White St. - MILE 12 is 25' before utility pole TMLP 33 on White St.
RIGHT onto Elizabeth Dr. - 20 K is 8'6" before utility pole TMLP7 on Elizabeth Dr.
RIGHT onto Mark Dr.;
LEFT onto Titicut Rd. -MILE 13 is 67' before near edge of drain cover on left side of road prior to main entrance of Raynham Middle School on Titicut Rd.
Bear LEFT onto School main access road to FINISH as per FINISH DETAIL

Start

34'1" before (north of) center line pavement seam of walkway to Raynham Middle School building door # 16 on main access road on the west side of the school.
Marked with PK nail, washer and paint

Finish

Even with lamp post on the left hand side of the main access road at the southwest corner of the Raynham Middle School main entry way, across from building door # 17 - 68 ft, 3 in before leading edge of storm grate on left (south) side of road. Marked with PK nail, washer and paint

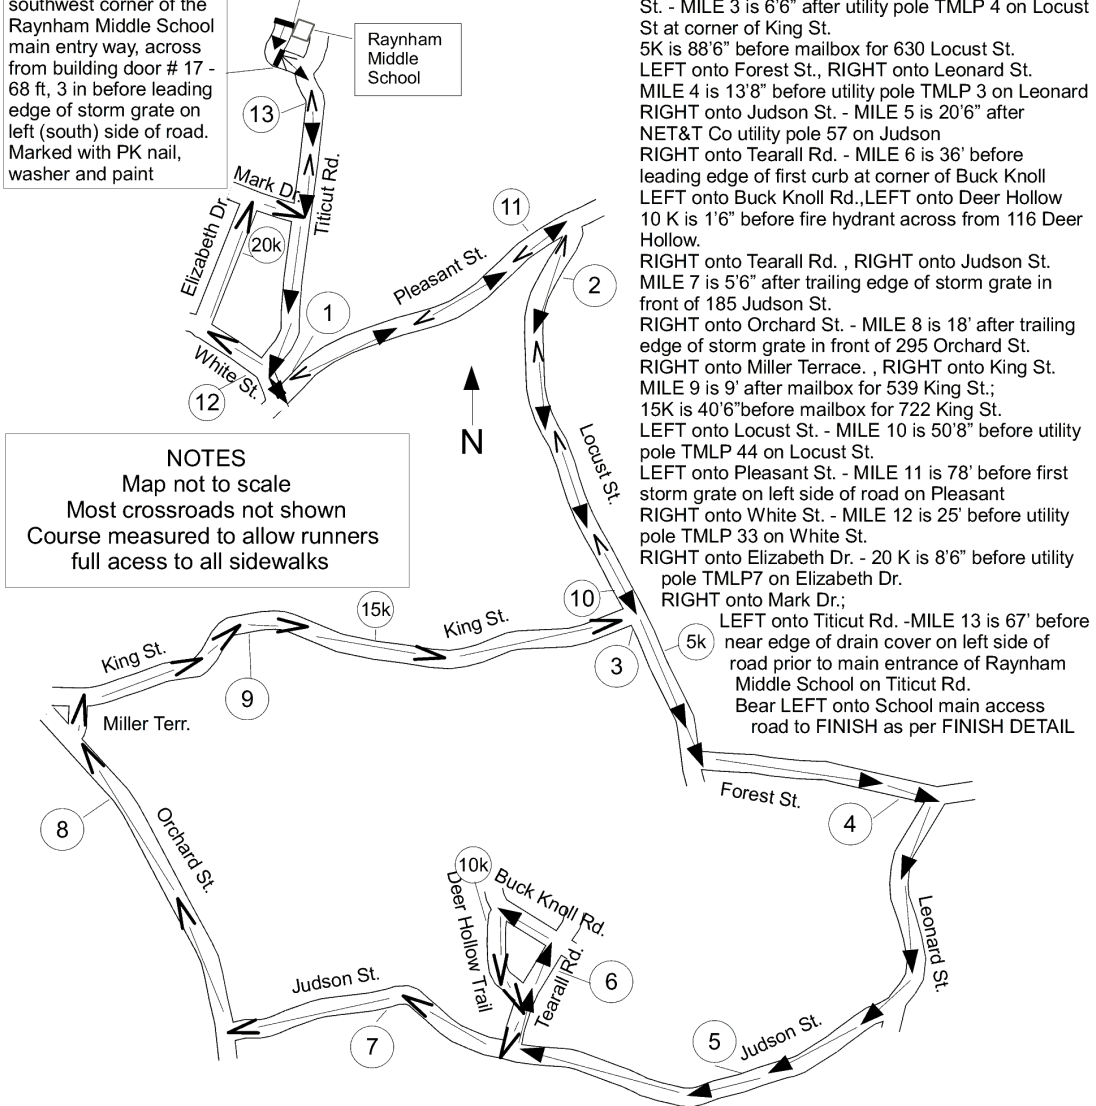

NOTES
Map not to scale
Most crossroads not shown
Course measured to allow runners full access to all sidewalks



USATF Certification #MA17037JK
Effective 11/24/2017 - 12/31/2027
Drop 0.07 m/Km, Separation 0.30%



*Road Running Technical Council
USA Track & Field*

Measurement Certificate



Name of the course Colonial Road Runners Frosty Half-Marathon Distance 21.0975 km
 Location (state) MA (city) Raynham
 Type of course: road race calibration course
 Measuring method: bicycle steel tape electronic distance meter
 Measured by (name, address, phone & e-mail) Mark Capparella, 30 Scott Hill Blvd, Bellingham, MA 02019
508-740-7836; mark_capparella@waters.com
 Race contact (name, address, phone & e-mail) John M. Donahue, 195 Hickory Dr, Raynham MA 02767
617-620-1246; john.donahue64@gmail.com
 Date(s) when course measured: Nov 17, 2017
 Number of measurements of entire course: 2 Course Configuration: keyhole
 Elevation (meters above sea level) Start 26.0 m Finish 24.6 m Highest 42.5 m Lowest 7.9 m
 Straight line distance between start & finish 0.0628 km Drop 0.07 m/km Separation 0.30 %
 Type of surface: paved 100 % dirt - % gravel - % grass - % track - %
 Effective date of certification: Nov 24, 2017 Certification code: MA17037JK

Notice to Race Director: Use this Certification Code in *all* public announcements relating to your race.

Be It Officially Noted That

Based on examination of data provided by the above named measurer, the course described above and in the map attached is hereby certified as reasonably accurate in measurement according to the standards adopted by the Road Running Technical Council. If *any* changes are made to the course, this certification becomes void, and the course must then be recertified.

Verification of Course — In the event a National Open Record is set on this course, or at the discretion of USA Track & Field, a verification remeasurement may be required to be performed by a member of the Road Running Technical Council. If such a remeasurement shows the course to be short, then all pending records will be rejected and the course certification will be cancelled.

This certification expires on December 31 in the year 2027

AS NATIONALLY CERTIFIED BY:

Justin Kuo

Date: Nov 27, 2017

Justin Kuo • USATF/RRTC Course Certifier • 39 Oakland Road, Brookline, MA 02445-6700
 Phone: 617-731-9889 • Fax: 617-939-0992 • Email: jkuo@usatfne.org
