

**The Bank of America
Chicago Marathon
Chicago, IL USA**



USATF Certificate IL18025NM
Effective
Jun. 29, 2018 - Dec. 31, 2028

START: Northbound Columbus Dr, mag nail,
E curb Columbus Dr, 10.5' N of light pole C101 -
at SE corner of Columbus & Monroe,
just S of Monroe.

Certified splits:


25 km: E edge Damen, 2' 10" N of 2nd light pole -
S of SE corner of Damen & Adams.

30 km: Mid intersection, 33' 8" S of fire-hydrant at -
NW corner of Loomis & Washburne.

35 km: E curb of Wentworth median,
84' S of 1st light pole S of overpass, just S of 24th Pl.

40 km: E edge Michigan,
61' 6" N of fire-hydrant in-front of 2235 Michigan.

FINISH: Northbound Columbus Dr, mag nail,
W curb Columbus Dr, 37' 4" S of light pole C1010.

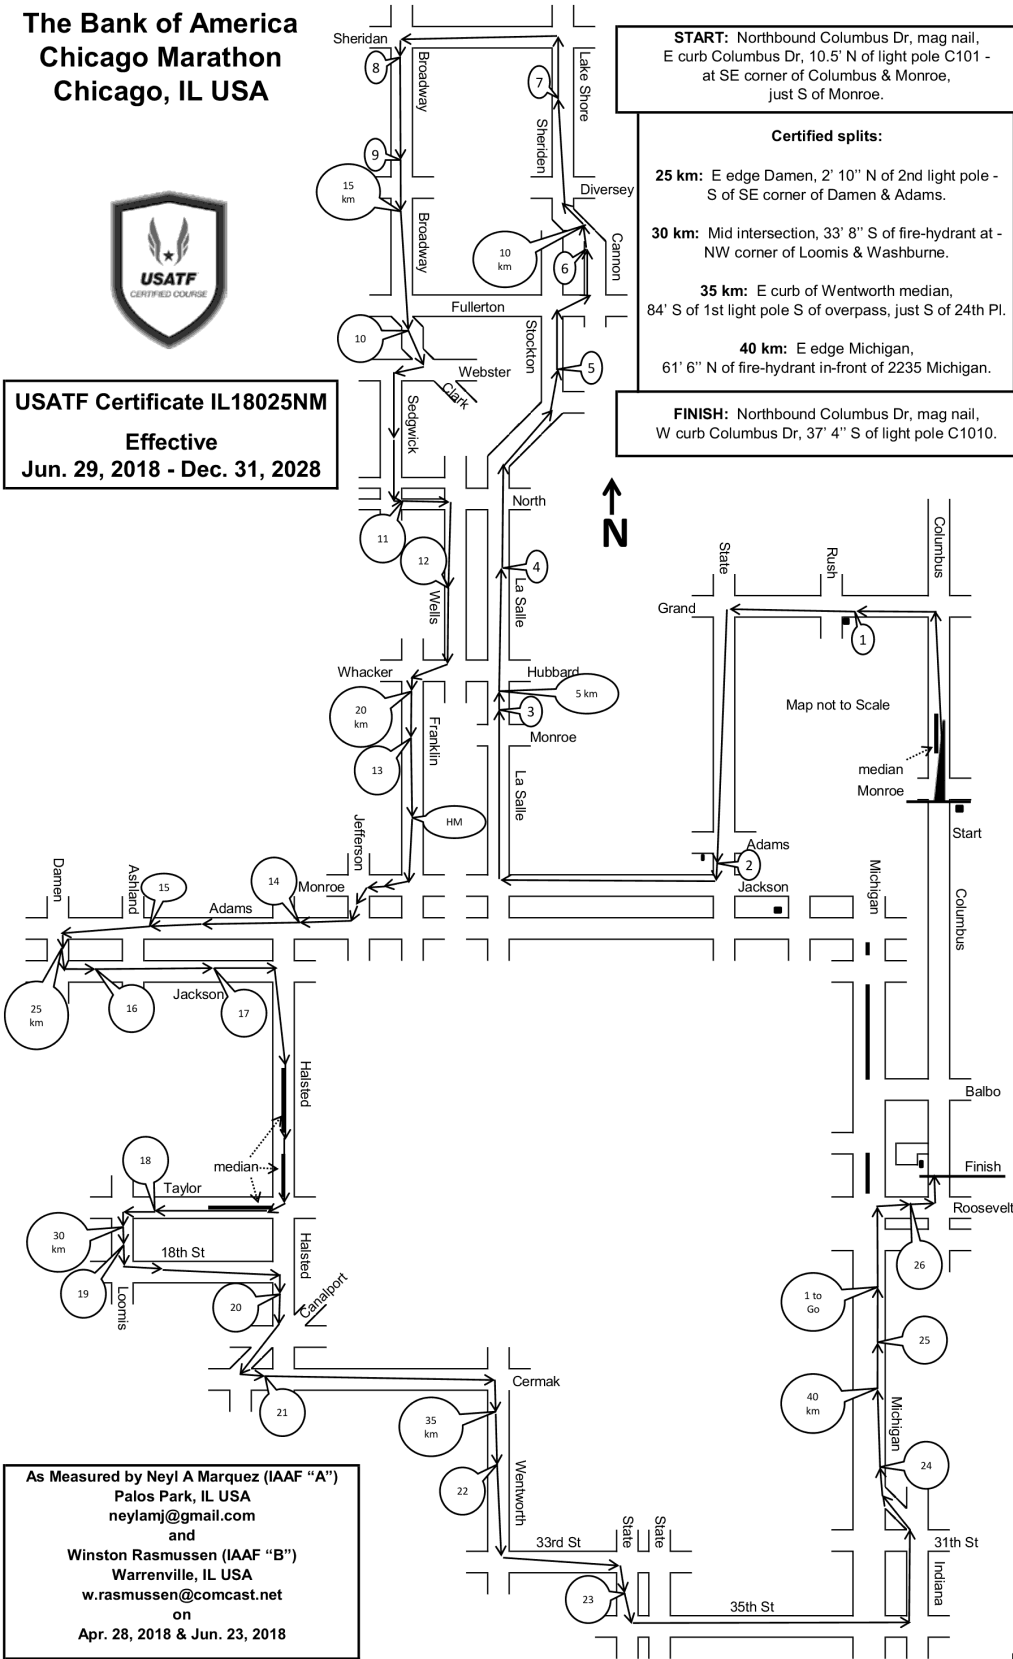

As Measured by Neyl A Marquez (IAAF "A")
Palos Park, IL USA
neylamj@gmail.com
and
Winston Rasmussen (IAAF "B")
Warrenville, IL USA
w.rasmussen@comcast.net
on
Apr. 28, 2018 & Jun. 23, 2018



Road Running Technical Council
USA Track & Field

Measurement Certificate

recognized by



Name of the course The Bank of America Chicago Marathon
(with certified splits: 25 km, 30 km, 35 km, 40 km) Distance 42.195 km

Location (state) IL (city) Chicago

Type of course: road race calibration course

Measuring method: bicycle steel tape electronic distance meter

Measured by (name, address, phone & e-mail) Neyl A Marquez (IAAF "A"), Palos Park, IL USA, (312) 933 3796, neylamj@gmail.com & Winston Rasmussen (IAAF "B"), Warrenville, IL USA, (630) 930 9341, w.rasmussen@comcast.net

Race contact (name, address, phone & e-mail) Carey Pinkowski, 135 South LaSalle Street, Suite 1160, Chicago, IL 60603, (312) 904 9802, carey.pinkowski@bankofamerica.com

Date(s) when course measured: Apr. 28, 2018 & Jun. 23, 2018

Number of measurements of entire course: 2 Course Configuration: Partial Loop

Elevation (meters above sea level) Start 182 m Finish 184 m Highest 184 m Lowest 176 m

Straight line distance between start & finish 1230 m Drop -0.05 m/km Separation 2.92 %

Type of surface: paved 100 % dirt % gravel % grass % track %

Effective date of certification: Jun. 29, 2018 Certification code: IL18025NM

Certified Splits: km, EL ST, FIN, High, Low, Straight line distance ST & FIN, Drop, Separation
25 km, 182 m, 180 m, 183 m, 176 m, 4640 m, 0.08 m/km, 18.56%
30 km, 182 m, 180 m, 183 m, 176 m, 3770 m, 0.07 m/km, 12.57%
35 km, 182 m, 181 m, 183 m, 176 m, 3810 m, 0.03 m/km, 10.89%
40 km, 182 m, 181 m, 183 m, 176 m, 3159 m, 0.03 m/km, 7.88%

Notice to Race Director: Use this Certification Code in **all** public announcements relating to your race.

Be It Officially Noted That

Based on examination of data provided by the above named measurer, the course described above and in the map attached is hereby certified as reasonably accurate in measurement according to the standards adopted by the Road Running Technical Council. If **any** changes are made to the course, this certification becomes void, and the course must then be recertified.

Verification of Course — In the event a National Open Record is set on this course, or at the discretion of USA Track & Field, a verification remeasurement may be required to be performed by a member of the Road Running Technical Council. If such a remeasurement shows the course to be short, then all pending records will be rejected and the course certification will be cancelled.

This certification expires on December 31 in the year 2028

AS NATIONALLY CERTIFIED BY:

 Date: Jul. 1, 2018
Neyl A Marquez | USATF/RRTC Certifier & IAAF-AIMS Course Measurer (A)
7925 West Palos Ave, Palos Park, IL 60464 | +1 312 933 3796 | neylamj@gmail.com

IL18025NM - p. 7 of 7

42 km: W edge Columbus, 32' 4" N of streetlight/traffic light pole just N of crosswalk at NW corner of Columbus and Roosevelt.

FINISH: Northbound Columbus Dr, mag nail, W curb Columbus Dr, 37' 4" S of light pole C1010.

17 km: E edge Sedgewick, 71' S of fire-hydrant across from 1928 Sedgewick.

18 km: W edge Wells, 25' S of traffic light at SW corner of Wells & North Ave.

19 km: W edge Wells, 22' S of Chicago WW manhole cover at middle of road, just S of Hill.

20 km: W edge Wells, 56' 4" S of traffic light at SW corner of Wells & Ontario.

21 km: E edge Franklin, 83' 9" S of watermain at 160-162 Franklin.

Half Marathon: W edge Franklin, 4' S of fire-hydrant at NW corner of Franklin & Court.

22 km: S edge Monroe, 13' 7" E of watermain just W of 555 Monroe.

23 km: N edge Adams, 61' W of 2nd light pole W of SW corner of Adams & Morgan.

24 km: N edge Adams, 57' W of fire-hydrant at NW corner of Adams & Laflin.

25 km: E edge Damen, 2' 10" N of 2nd light pole S of SE corner of Damen & Adams.

26 km: S edge Jackson, 78' 10" W of fire-hydrant in-front of 1524 Jackson.

27 km: S edge Jackson, 5' 11" W of watermain at 1041 Jackson.

28 km: Northbound lanes of Halsted, middle of road, 50' 4" N of fire-hydrant (W edge) S of Harrison.

29 km: S edge Taylor, 6' 6" E of Al's honorary street pole (Brown) at parking lot entrance to restaurant.

30 km: Mid intersection, 33' 8" S of fire-hydrant at NW corner of Loomis & Washburne.

31 km: N edge 18th St, 7' E of Chicago Sewer manhole cover in middle of street between 1327 & 1328 18th St.

32 km: S edge 18th St, 11' 4" E of Chicago Sewer manhole cover just E of 1801 18th St.

33 km: N edge Cermak, 142' 6" E of fire-hydrant E of NE corner of Cermak & Canalport.

34 km: N edge Cermak, under bridge, 3' E of the west-end of 1st bridge W of Archer.

35 km: E curb of median, 84' S of 1st light pole S of overpass, just S of 24th Pl.

36 km: W edge Wentworth, 3' 2" N of light pole in-front of 3036-3024 Wentworth.

37 km: W edge State, 60' 4" N of 1st fire-hydrant N of 34th St, between crosswalks.

38 km: W edge Indiana, 14' 6" S of light pole at SW corner of Indiana & 33rd Blvd.

39 km: E edge Michigan, 11' 8" S of 3rd light pole S of 28th St.

40 km: E edge Michigan, 61' 6" N of fire-hydrant in-front of 2235 Michigan.

41 km: E edge Michigan, 76' N of overpass N of 16th St.

The Bank of America Chicago Marathon

Chicago, IL US

List of Intermediate Measured Kilometer Points

As Measured by Neyl A Marquez (IAAF "A"), Palos Park, IL USA

and

Winston Rasmussen (IAAF "B"), Warrenville, IL USA

on

Apr. 28, 2018 & Jun. 23, 2018

START: Northbound Columbus Dr, mag nail, E curb Columbus Dr, 10.5' N of light pole C101 at SE corner of Columbus & Monroe, just S of Monroe.

1 km: W edge Columbus, 29'6" N of traffic light at NW corner of Columbus & North Water St.

2 km: E edge State, 41' 9" N of fire-hydrant at NE corner of State & Hubbard.

3 km: W edge State, 2' S of Chicago WW manhole cover in-front of 26-28 Michigan.

4 km: E edge LaSalle, 59' N of traffic light at NE corner of LaSalle & Monroe.

5 km: E edge LaSalle, 4' 6" N of fire-hydrant at SE corner of LaSalle & Hubbard.

6 km: E edge LaSalle, 56' 6" S of light pole at SE corner of LaSalle & Delaware.

7 km: E edge LaSalle, 45' N of fire-hydrant at NE corner of LaSalle & Schiller.

8 km: W edge Stockton, 5' N of CTA Bus Stop (W edge), just S Farm in the Zoo.

9 km: E curb Stockton, 21' 9" S of 3rd light pole S of SE corner of Stockton & Fullerton.

10 km: W edge Cannon, 7' 6" S of 2nd light pole at SE of Stockton.

11 km: W edge Lake Shore Dr, 38' 5" N of traffic light at NW corner of Lake Shore Dr & Belmont.

12 km: W edge Lake Shore Dr, 21' 9" N of traffic light at NW corner of Lake Shore Dr & Addison.

13 km: W edge Broadway, 8' 3" N of light pole BR3759 at NE corner of Broadway & Grace.

14 km: E edge Broadway, 4' N of light pole at NW corner of Broadway & Buckingham.

15 km: W edge Broadway, 24' N of fire-hydrant in-front of 2835 Broadway.

16 km: E edge Clark, 15' 5" S of traffic light at NW corner of Clark & Fullerton.

20 km: W edge Wells, 56' 4" S of traffic light at SW corner of Wells & Ontario.

13 mi.: E edge Franklin, 46' 3" S of fire-hydrant at SW corner of Franklin & Lake.

Half Marathon: W edge Franklin, 4' S of fire-hydrant at NW corner of Franklin & Court.

14 mi.: N edge Adams, 32' E of City manhole cover NE corner of Adams & Halsted.

15 mi.: Mag nail, 7' 10" S of N curb and 29' 11" E of Chicago WW manhole cover at NE corner of Adams & Ashland.

25 km: E edge Damen, 2' 10" N of 2nd light pole S of SE corner of Damen & Adams.

16 mi.: N edge Jackson, 30' 1" E of manhole cover, middle of street, at 1640 Jackson parking entrance.

17 mi.: S edge Jackson, 14' 8" E of watermain at 847 Jackson.

18 mi.: S edge Taylor, 42' 9" W of fire-hydrant at NW corner of Taylor & Carpenter.

30 km: Mid intersection, 33' 8" S of fire-hydrant at NW corner of Loomis & Washburne.

19 mi.: E edge Loomis, underneath bridge, 65' S of the N end of the 1st railroad bridge just S of 15th St.

20 mi.: W edge Halsted, 11' 5" S of light pole/Bus Stop sign in-front of 1826 Halsted.

21 mi.: N edge Cermak, 27' 6" East of gates of South Branch Chicago River bridge, W of Canal

35 km: E curb of Wentworth median, 84' S of 1st light pole S of overpass, just S of 24th Pl.

22 mi.: W edge Wentworth, 7' S of fire-hydrant at SW corner of Wentworth & 27th St.

23 mi.: W edge State, 7' 11" N of 1st fire-hydrant N of 34th St, between crosswalks.

24 mi.: E edge Michigan, 4' N of 4th light pole N of fire-hydrant at NE corner of Michigan and 31st St.

40 km: E edge Michigan, 61' 6" N of fire-hydrant in-front of 2235 Michigan.

25 mi.: E edge Michigan, 12' 9" N of light pole at SE corner of Michigan & 21st St.

1 mi. To Go: E edge Michigan, 37' 9" N of fire-hydrant across from 1823 Michigan.

26 mi.: N edge Roosevelt, 7' 4" E of Chicago Sewer manhole cover at NE corner of Roosevelt & Indiana.

FINISH: Northbound Columbus Dr, mag nail, W curb Columbus Dr, 37' 4" S of light pole C1010.

The Bank of America Chicago Marathon

Chicago, IL USA

List of Intermediate Measured Points

As Measured by Neyl A Marquez (IAAF "A"), Palos Park, IL USA

and

Winston Rasmussen (IAAF "B"), Warrenville, IL USA

on

Apr. 28, 2018 & Jun. 23, 2018

START: Northbound Columbus Dr, mag nail, E curb Columbus Dr, 10.5' N of light pole C101 at SE corner of Columbus & Monroe, just S of Monroe.

1 mi.: S edge Grand, 30.5' E of fire-hydrant at SE corner of Grand & Rush, just E of Rush.

2 mi.: W edge State, 35' S of traffic light pole at SW corner of State & Adams.

3 mi.: E edge LaSalle, 47' 6" N of fire-hydrant in-front 333 LaSalle bldg.

5 km: E edge LaSalle, 4' 6" N of fire-hydrant at SE corner of LaSalle & Hubbard.

4 mi.: E edge LaSalle, 46' 8" S of fire-hydrant at SE corner of LaSalle & Elm.

5 mi.: E edge Stockton, 30' 6" S of service entrance to Farm in the Zoo.

6 mi.: W edge Cannon, 25' S of 1st fire-hydrant (E side) S of Diversey Harbor Boat Launch entrance.

10 km: W edge Cannon, 7' 6" S of 2nd light pole at SE of Stockton.

7 mi.: W edge, Lake Shore Dr local lanes, 38' N of center of Chicago Sewer grate in-front of entrance to 3300 Lake Shore Dr.

8 mi.: E edge Broadway, 14' S of 2nd light pole BR3834 (W side) S of Sheridan.

9 mi.: W edge Broadway, 18' S of watermain between 3126 & 3128 Broadway.

15 km: W edge Broadway, 24' N of fire-hydrant in-front of 2835 Broadway.

10 mi.: W edge Clark, 18' S of light pole in-front of 2345 Clark.

11 mi.: N curb of North Ave median, 52' E of City Electrical manhole cover at median just E of Sedgwick.

12 mi.: W edge Wells, 21' N of light pole at NW corner of Wells & Locust.
